



DHAMMA VINAYA MONASTERY PROJECT

KHADAKWASLA , PUNE





PROJECT UPDATES

SITE PHASE WISE ZONING



PHASE I ■

MONASTERY WING:
STUPA
ADMIN BLOCK, MEDITATION HALL
MONKS RESIDENCE UPOSATH HALL
GURUJIS RESIDENCE

PHASE II ■

JETWAN RESIDENCES
VIPASSANA CENTRE

PHASE III ■

WOMEN EMPOWERMENT CENTRE
MANAGEMENT DEVELOPMENT CENTRE

WATER BODY ■

ROAD ■

DHAMMA V

MONASTERY COMPLEX

LEGEND

I. ANCILLARY AMENITIES


1. MAIN SITE ENTRANCE PLAZA
2. PARKING LOT
3. CANTEEN AND TOILETS

II. STUPA COMPLEX

4. MINI TEMPLE
5. BODHI VRUKSHA
6. STUPA ENTRANCE GATEWAYS
7. MAIN STUPA
8. LANDSCAPED GARDENS

III. MONASTERY COMPLEX

- A. MONASTERY ENTRY AND PARKING
- B. MONASTERY ADMIN BLOCK
- C. CHANTING AND MEDITATION HALL
- D. MONK QUARTERS
- E. UPOSATHA HALL
- F. MAIN ABBOT'S QUARTERS
- G. FOREST GROVE

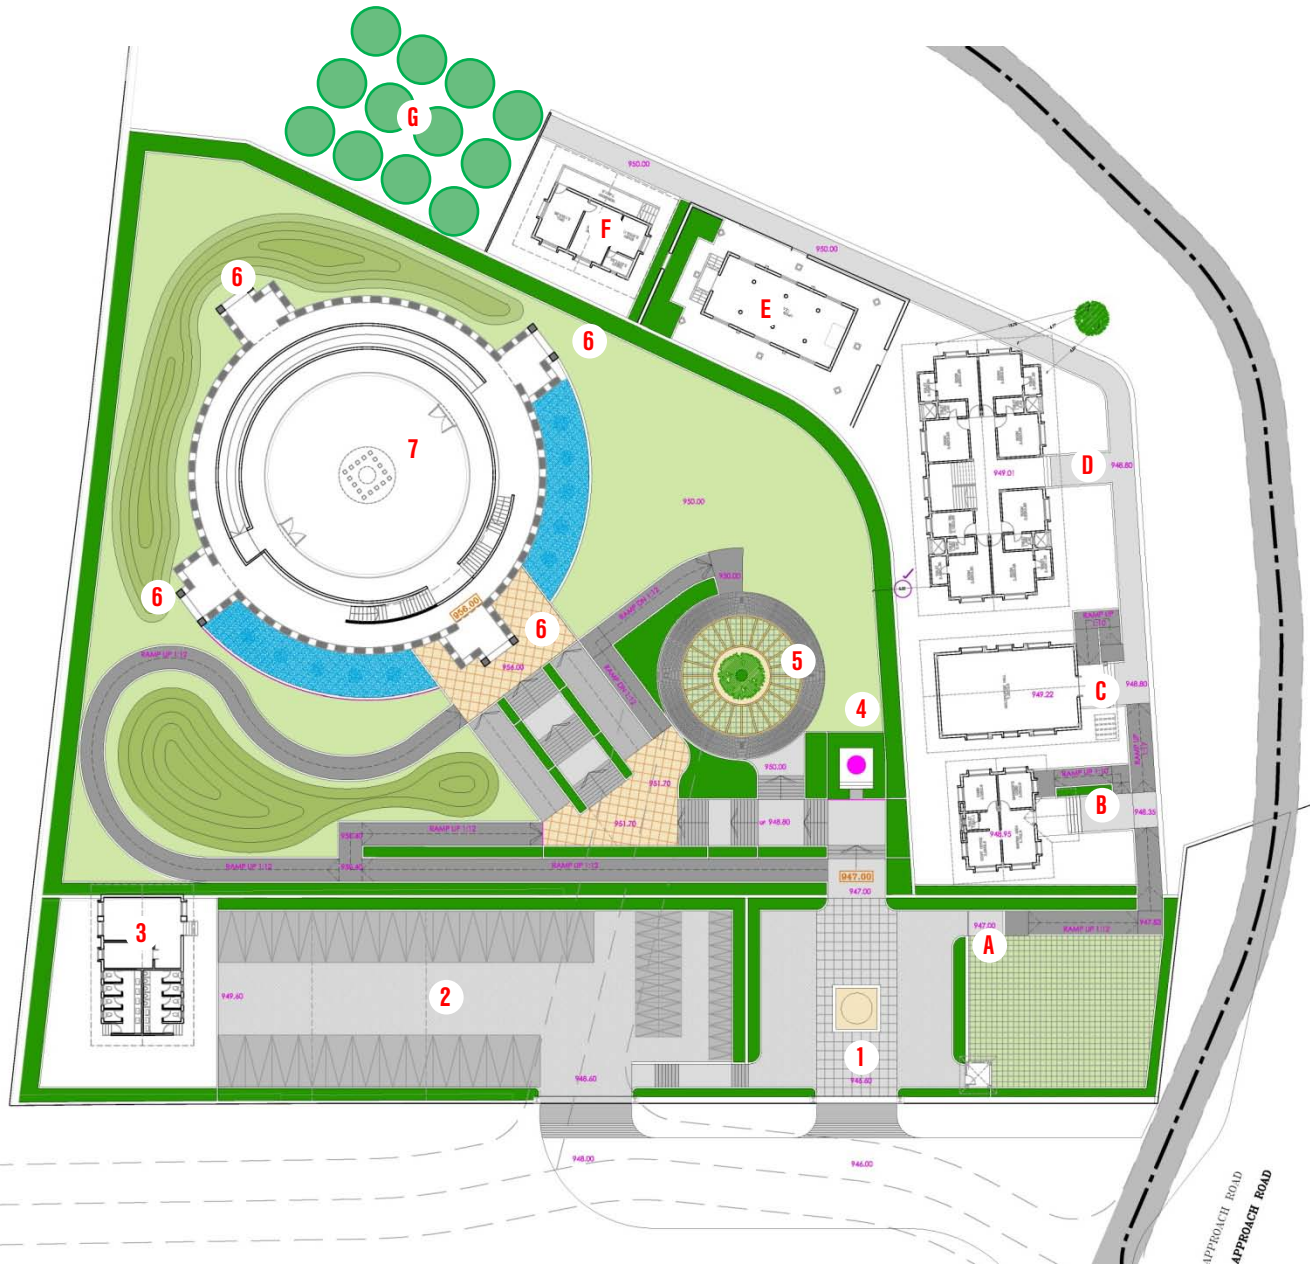

MONASTERY COMPLEX



Aerial view

STUPA





SITE PROGRESS IMAGES

INITIATION OF WORK



5 February 2020

STUPA



GURUJI'S RESIDENCE



MONK'S RESIDENTIAL BLOCK



MEDITATION HALL & ADMINISTRATION BLOCK



FIRST VIPASSANA ONE DAY COURSE AT DVMP MEDITATION HALL



WORK STATUS

STUPA

WORK COMPLETED

RCC STRUCTURE- DOME AND
BASEMENT HALL

WORK TO BE COMPLETED

HARMIKA- THE TOP RAILING AND
CHATRI , RAILING, STONE CLADDING,
BASE DOME, TORANAS- THE GATES,
RAMP, CIRCUMBULATORY PATH
RAILING, PAVEMENT AND SITE
INFRASTRUCTURE

WORK STATUS

MONASTERY WING

WORK
COMPLETED

WORK TO BE
COMPLETED

GURUJI'S RESIDENCE

RCC FRAME WORK IN PROGRESS

BLOCK WORK , FINISHING

UPOSATH HALL

FOUNDATION AND PLINTH

COLUMN BEAMS, BLOCK
WORK, FINISHING

RESIDENCE FOR MONKS

FOUNDATION AND PLINTH

FIXING OF WINDOWS

MEDITATION HALL

COMPLETED

ADMIN BLOCK

COMPLETED

EXPECTED COMPLETION TIMELINE

STUPA	DEC 2022
GURUJI'S RESIDENCE	JUNE 2022
UPOSATH HALL	DEC 2022
RESIDENCE FOR MONKS	JUNE 2022
MEDITATION HALL	COMPLETED
ADMIN BLOCK	COMPLETED
